

# COMMUNITY REDEVELOPMENT AGENCY PROJECT PROGRESS REPORT NOVEMBER 13, 2024 CRA MEETING



### CRA Projects:

Project Name	Page/Slide No.
4642 Vincennes Boulevard Parking Lot	3
4813 Vincennes Street Parking Lot	5
Big John's Parking Lot Improvements	7
Dumpster Façade	9
Replacement of Dumpsters to Compactors	11
Country Club Boulevard Median Landscaping	13
Palm Tree Blvd. Median Landscaping Project	15
SE 47th St Area CRA Improvement Project	17
Miramar Street Sidewalks	19
Cape Coral Pkwy Street Light Retrofit	21
Decorative Lighting on Cape Coral Pkwy. & SE 47 <sup>th</sup> Ter	23
Wastewater System Improvements	25
Utility Box Public Art Project	27
Bimini Basin Mooring Field	29
SE 47 <sup>th</sup> Terrace Fire Department Fire Connections	. 31
Palm Tree Public Square	33
Old Golf Course	35
Bimini East	37
The Cove at 47 <sup>th</sup>	39
Bimini Square	41
Breaking Barriers To Business (B2B)	43
Demolition Program	44



## 4642 Vincennes Boulevard Public Parking

Project Number: C193001007 Estimated Completion Date: Summer 2025

**Scope of Work:** 4642 Vincennes Blvd. (North of Cape Coral Parkway)

Design and construct of a 40-space parking lot to include landscaping, curbing, paving,

drainage inlets and lighting.

**Approved Budget:** \$659,591 **Expenditures to Date:** \$56,290

#### **Completed Tasks:**

July Awaiting final signatures on SCP amendment

August SCP Amendment #2 has been in review by legal and procurement.

Notification was received on 8/22 that the SCP Amendment and Memo has

been completed and is awaiting final signatures.

Sept. Ammendment #2 was signed and approved. The consultant has started work

on the additional work design.

Oct. Design of additional work is almost complete. A new site lighting spec has

been proposed and new electrical service requirements for the EV Charger.



# 4642 Vincennes Boulevard Public Parking







## 4813 Vincennes Street Public Parking

Project Number: C193001007 Estimated Completion Date: Summer 2025

Scope of Work: 4813 Vincennes St. (South of Cape Coral Parkway)

Design and construct of a 20-space parking lot to include landscaping, curbing, paving,

drainage inlets and lighting.

**Approved Budget:** \$371,020 **Expenditures to Date:** \$0

#### **Completed Tasks:**

Mar/Apr Completed SOW and updating cost estimate. RFS submitted.

May Working with CPH to develop SCP.

June Reviewing SCP.

July SCP approved in the amount of \$57,937.


Aug CPH survey crew started field work on Aug 8th.

Sept Survey work completed; Project Design has begun.

Oct Design near completion, 23 Spaces including 2 ADA spaces.



# 4813 Vincennes Street Public Parking

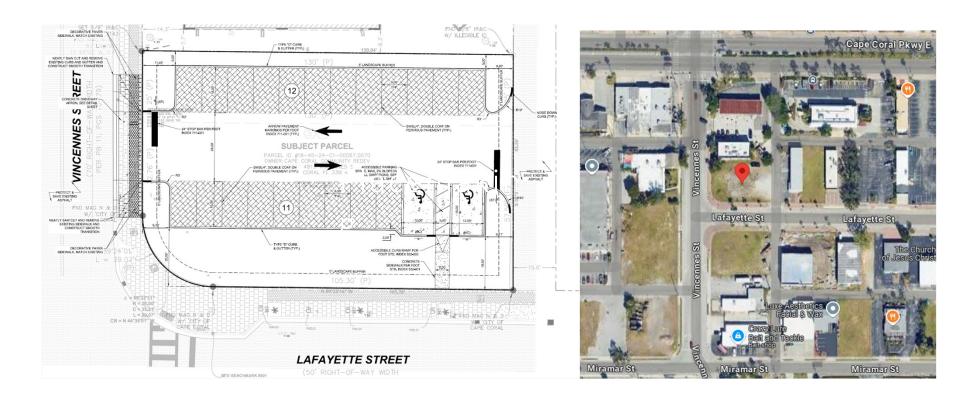



## Big Johns Parking Lot Improvements

Project Number: C193001011 Estimated Completion Date: Summer 2025

**Scope of Work**: Mil and resurface Big John's parking lot with the addition of Compactors

and EV chargers. Restripe and addition of speed bumps.

**Approved Budget:** \$1,560,082 **Expenditures to Date:** \$0

#### **Completed Tasks:**

May Creating SOW to include compactor enclosures and speedbumps.

June Continuing to work on SOW.

July SOW completed working with procurement for design.

Aug SOW completed, RFS on design submitted to Procurement.

Sept RFS approved working with CPH on SCP.

October Site visit with CPH to complete SCP.



# Big Johns Parking Lot Improvements









## **Dumpster Enclosure**

Project Number: C193001011 Estimated Completion Date: Summer 2025

**Scope of Work:** Improvements to dumpster enclosers including steel powder coated gates

and concrete shiplap walls.

### **Completed Tasks:**

Mar/Apr Currently assessing trash volume to determine the amount of space needed

for dumpster enclosures.

May Enclosure concepts received. Working with Waste Pro on compactor sizing.

June Wastepro is finalizing pricing and specs for compactors.

July Project estimates shared with Finance for budget. Project to begin with

compactor enclosures.

Aug SOW completed for Big Johns, RFS on design submitted to Procurement.

Sept RFS approved working with CPH on SCP.

October Site visit with CPH to confirm compactor locations and service connections

for SCP.

Project Lead: Zachary Gogel, Project Manager/CRA

# Dumpster Enclosure





## Replacement of Dumpsters to Compactors

**Project Number:** C193001015 **Estimated Completion Date:** Summer 2025

Scope of Work: Replace dumpsters with compactors in serval areas to increase parking

spaces.

**Approved Budget:** \$370,000 **Expenditures to Date:** \$0

#### **Completed Tasks:**

Mar/Apr Currently assessing trash volume to determine compactor locations.

May Working with Waste Pro on compactor sizing.

June Wastepro is finalizing pricing and specs for compactors.

July Project estimates shared with Finance for budget. Project to begin with

Big John's parking lot.

Aug SOW completed for Big Johns, RFS on design submitted to Procurement.


Sept RFS approved working with CPH on SCP.


October Site visit with CPH to confirm compactor locations and service connections

for SCP.



# Replacement of Dumpsters to Compactors

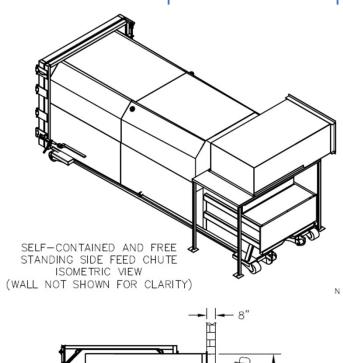





## Country Club Boulevard Median Landscaping

**Project Number:** C193001005 **Estimated Completion Date:** Spring 2025

**Scope of Work:** Country Club Blvd from Palm Tree Blvd to Wildwood Pkwy.

Consultant to prepare transportation and median design plans including access management. The work will be followed by landscape and irrigation plans.

**Approved Budget:** \$800,000 **Expenditures to Date:** \$76,145

## **Completed Tasks:**

May Scheduling public input meeting for July. Anticipated 60% design to be in

July.

June Redesigning plans for Palm Tree medians south of Country Club.

July Redesign completed working to submit RFW. Public input meeting scheduled

for August 14<sup>th</sup>.

Aug RFW submitted, finalizing bid documents for curbing on Palm Tree Blvd

medians South of Country Club Blvd.

Sept 90% plans received for landscaping design.

October Bid for Palm Tree medians south of Country Club to open on November 6<sup>th</sup>

and close on December 10<sup>th</sup>.

Project Lead: Zachary Gogel, Project Manager/CRA

# Country Club Boulevard Median Landscaping





## Palm Tree Blvd. Median Landscaping Project

**Project Number:** C193001012 **Estimated Completion Date:** Fall 2025

**Scope of Work:** Palm Tree Blvd from Country Club Blvd to Wildwood Pkwy.

Consultant to prepare transportation and median design plans including access management. The work will be followed by landscape and irrigation plans.

**Approved Budget:** \$1,334,961 **Expenditures to Date:** \$0

#### **Completed Tasks:**

May Internal meeting to discuss SCP from Stantec on 6/5/24.

June Meeting with Stantec scheduled for 6/13/24.

July Working with procurement to approve SCP.

Aug SCP for design services to be presented for approval at the

September 11<sup>th</sup> CRA meeting.

Sept PO issued design services has begun.

October Stantec is working on Design Task 1 Corridor Analysis and Report.



# Palm Tree Blvd. Median Landscaping Project





## SE 47th St Area CRA Improvement Project

**Project Number:** C193001008 **Estimated Completion Date:** Spring 2025

**Scope of Work:** Design improvements to the streetscape including trees, concrete,

pavers, and other items. Location is East of Del Prado Blvd.

**Approved Budget:** \$216,818 **Expenditures to Date:** \$0

#### **Completed Tasks:**

Aug RFS submitted for Design on August 22<sup>nd</sup>.

Sept RFS approved creating SCP with KCI Technologies, INC.

October Negotiating terms of SCP.



# SE 47th St Area CRA Improvement Project





#### Miramar Street Sidewalks

**Approved Budget:** \$413,200 **Expenditures to Date:** \$229,326

#### **Completed Tasks:**

August Project very close to being completed. No change to report.

September Vault lid to be replaced before finial section is poured, waiting for PO to be

issued from Procurement.

October Issued a PO to Restoration & Protective Solutions. Piping to be replaced in

mid November with vault lid shortly after. Project to be completed by second

week of December once sidewalk is constructed.



# Miramar Street Sidewalks





## Cape Coral Pkwy Streetlight Retrofit

**Project Number:** C193001013 **Estimated Completion Date:** Spring 2025

**Scope of Work:** To improve the streetlight reliability by upgrading the electrical

infrastructure and replacing the green streetlights along Cape Coral Pkwy.

**Approved Budget:** \$924,824 **Expenditures to Date:** \$0

#### **Completed Tasks:**

June Received specs for painting traffic signal poles. Applying specs to SOW.

July Reviewing project needs with changing of streetlight poles.

Aug Reappropriated the funds from the Repainting of Signal Poles to the Cape

Coral Pkwy Street Light Retrofit. RFS submitted for Photometrics of the green decorative streetlights on Cape Coral Pkwy from Palm Tree Blvd to

Del Prado Blvd.

Sept RFS approved, creating SCP with Matern.

October SCP submitted to Procurement for review.



# Cape Coral Pkwy Street Light Retrofit







## **Decorative Tree Lighting**

Scope of Work: Provide year-round decorative lighting on Cape Coral Pkwy. from Coronado

Pkwy. To Del Prado Blvd. and on SE 47th Terrace from Coronado Pkwy. To SE 15th Ave.

Lighting will be hardened by changing to low-voltage as a way reduce sensitivity to moisture.

**Approved Budget:** \$160,000 **Expenditures to Date:** \$22,000

#### **Completed Tasks:**

Jan/Feb Decorative lights operational; project complete

Mar/Apr Testing three new low-voltage options to identify the best one going forward.

May Continuing testing at City Hall.

June Continuing testing at City Hall.

July No changes to report

Aug New lights will be purchased in September. Install on CCPKWY to be

completed by mid to late November.

Sept Obtaining quotes for light purchase.

October Installation of infrastructure has begun.

Project Lead: Eric Olive, Sr. Electrician/PW

# Decorative Tree Lighting









## Wastewater System Improvements

**Project Number:** C36401039 **Estimated Completion Date:** Spring 2025

**Scope of Work:** In 2021, Council approved a contract for professional engineering design services for Master Pump Station (MPS) 100 and force main transmission lines (FMTL). Construction on MPS 100 is underway, and the force main transmission lines are complete.

**Approved Budget:** \$1.78 million (Design) **Expenditures to Date:** \$1.28 million \$7.08 million (FMTL) \$5.42 million

\$13.09 million (Site) \$4.61 million

#### **Completed Tasks:**

Sept/Oct Milling and paving one side of SE 47<sup>th</sup> Terr road crown to the edge of

pavement was completed in March 2024

Nov/Feb Force Main and paving has been completed.

July Site Construction on MPS-100 is 25% complete.


August Site Construction on MPS-100 is 30% complete.

September Site Construction on MPS-100 is 30% complete.

October Site Construction on MPS-100 is 35% complete.



# Wastewater System Improvements

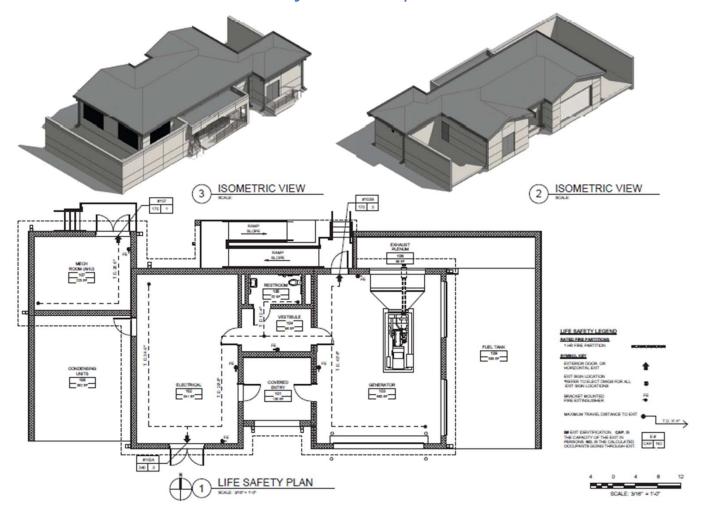



## Utility Box Public Art Project

**Estimated Completion Date:** Spring 2025

**Scope of Work:** Identifying Utility Boxes to wrap with artwork within the CRA.

**Approved Budget:** \$9,000 **Expenditures to Date:** \$0

#### **Completed Tasks:**

Jan/Feb On hold - Artwork being moved to other locations.

Mar/Apr Identify unwrapped utility boxes for artwork to be installed.

May New utility boxes around The Cove at 47<sup>th</sup> to be wrapped.

June Waiting for The Cove to remove fencing to begin project.

July Fencing at The Cove has been removed, working to measure utility boxes.

Aug Using GIS to locate all utility boxes in the CRA to create a priority list of

those to be wrapped.

Sept Continuing to compile list.

October Working to wrap Utility Box at 1517 Cape Coral Parkway E.



# Utility Box Public Art Project







## Bimini Basin Mooring Field - Design and Permitting

**Scope of Work**: Design and permit a mooring field at the Bimini Basin. Ancillary improvements at Four Freedoms Park include: New seawall (with Captain's walk and connecting sidewalks), dinghy dock, pump out station, and a modular facility (with public/private restrooms, shower room, laundry/ice machine room, and an office/storage room).

**Approved Budget:** \$497,331 **Expenditures to Date:** \$108,573

#### **Completed Tasks:**

June/July Geotechnical report received. Seawall options discussed. Modular facility concept

design confirmed. Conversations with USACE regarding their permitting. Economic

Development working on timeline of project.

August No change to report.

September Seawall related plans received and under review. Meeting delayed due to

Hurricane Helene.

October Draft mooring field management plan, layout of pump out dock, and dinghy

dock plans received and under review. Meetings delayed due to Hurricane

Milton.

Project Lead: Chris Camp, Principal Engineer (Public Works - Property Management)

29

# Bimini Basin Mooring Field - Design and Permitting





## SE 47<sup>th</sup> Terrace Fire Department Fire Connections

Project Number: C193001003 Estimated Completion Date: Spring 2025

Scope of Work: Provide FDC assemblies at four select properties along the south side of

the Club Square parking lot.

**Approved Budget:** \$126,728 **Expenditures to Date:** \$0

#### **Completed Tasks:**

Mar Permits rejections addressed and submitted for review and approval.

Domestic backflow certification at Big Blue Brewing issue being addressed.

Apr Awaiting results of permit review. Project management being transferred to Zachary

Gogel, new CRA project manager.

May Working to find solution to contractor issue.

June Close to solution for the contractor issue.

July Had a site visit with a possible contractor to continue the work scoped by Summit

Fire. Identified deficiencies to be corrected with a possible change order.

Aug Total Fire to assume the contract from Summit.

Sept Total Fire to assume the contract from Summit.

Oct Summit signed Assumption of Contract for Total Fire.



# SE 47<sup>th</sup> Terrace Fire Department Fire Connections





## Palm Tree Public Square

Project Number: C193001016 Estimated Design Completion Date: Summer 2025

Scope of Work: Develop the roughly 1-acre parcel into a new park with landscaping, pedestrian

features, and a focal point fountain.

**Approved Budget:** \$377,737 **Expenditures to Date:** \$0

**Completed Tasks:** 

October Creating SOW for design concept of park.



# Palm Tree Public Square





#### **Old Golf Course**

Project Number: C193001006 (CRA Property Acquisition)

Scope of Work: CRA partially funded the purchase of the Old Golf Course located at 4003 Palm Tree

Blvd.

**Approved Budget for Purchase:** \$2,697,821 **Expenditures to Date:** \$0

#### **Current Tasks:**

- Species survey/wildlife assessment is out on the streets for consultants.
- Invasive tree contractor is already on board, just waiting for start date. Staff is currently working on a phased approach strategy.
- Staff is working on parking lot cleaning scope of work.
- Staff is working on a cart path assessment.
- Perimeter tree planting is being planned by staff.
- Old sign looking at options for refurbishment.
- Low mowing program to continue (13 mows per year). More during rainy season.



# Old Golf Course





#### Bimini East

Project Number: C190901001 Estimated Completion Date: Spring 2026

**Scope of Work:** The City plans to demolish 43 parcels located at the southwest quadrant of the intersection of Cape Coral Parkway and Coronado Parkway in the CRA's Bimini Basin District. These parcels, consisting of both improved and unimproved properties, cover approximately 18.73 acres. The purpose of the demolition is to prepare the site for future City development and use. The demolition will be performed and completed in accordance with all state, federal, and local regulations, as well as the specifications described in the attached scope and documents.


**Approved Budget:** \$40,279,504 **Expenditures to Date:** \$40,303,007

**Completed Tasks:** 

October Bid was opened on 10/08/2024 and closed on 10/25/2024.



## Bimini East

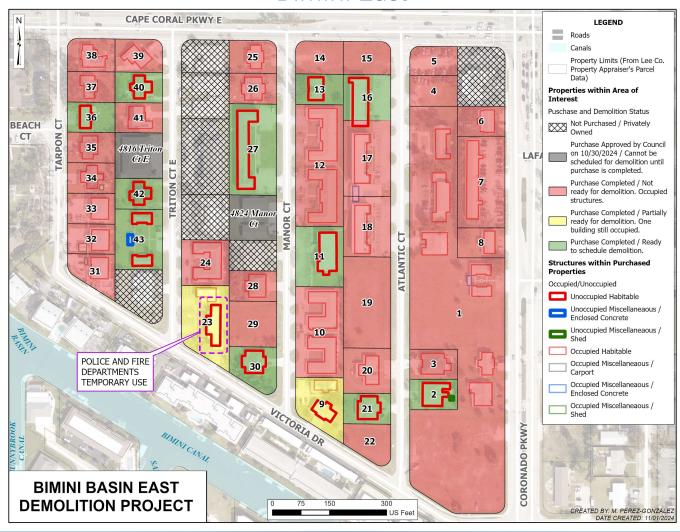



### Cove at 47th

**Estimated Completion Date:** Spring 2025

**Scope of Work:** Mixed-use multi-family private development with 290-units, 18k sq. feet of retail, 525-space parking garage (125 reserved for public). CRA contributing \$10.35 million for parking garage construction. CRA to work with developer on parking management system to create uniform parking system.

# **Approved Budget:** \$10.35 million **Advanced by the City - paying back annually Completed Tasks:**

July Apartments currently leasing. First 100 Units available for move-in August

16<sup>th</sup>.

August Phase 1 Residential (100 units) opening postponed to September. Garage opening

also set to open in September. Remaining phases anticipated to be substantially

complete by January 2025.

September Phase 1 Residential complete. 109 units open.

October Retail tenants to start build out of space in November. Tenants expected to begin

opening doors Q1 2025. Parking equipment installed and programming will be complete in November. Garage expected to go live early December. Full building

opening expected January 2025.



# Cove at 47th







## Bimini Square

**Estimated Completion Date:** Fall 2025

**Scope of Work:** Mixed-use multi-family development with 190 residential units, 47k sq. ft. medical office space for Lee Health, 7,500 sq. ft. waterfront restaurant, 27 boat slips, 3,000 sq. ft. Omelet House restaurant, 625 stall parking garage (125 public parking spaces). TIF Agreement calls for the CRA to transfer Increment Revenues into the Revenue Trust Fund as financial support. Off-site improvements (stormwater treatment and sewer line upgrade) are estimated to be \$3,210,953.

**Approved Budget:** not to exceed \$7 million **Expenditures to Date:** \$0

#### **Completed Tasks:**

July Three (3) residential buildings under construction. Commercial Building starting

structural steel.

August (3) residential buildings and commercial/mixed use under construction. Lee Health

permit still in review. City contract for ROW improvements being finalized.

September Framing for residential buildings and outpatient almost complete. Dry in/rooftop

complete for one out of three residential buildings.

October Framing and dry in being completed. Rough-in plumbing and electrical beginning.

Pouring for garage foundation partially poured. City Contract for ROW

improvements approved.

**Project Lead:** Sharon Woodberry, Economic Development Manager/CM

# Bimini Square





## Breaking Barriers To Business (B2B)

**Scope of Work:** The B2B Program is designed to provide grant assistance to developers and business owners in need of funding assistance to meet requirement of the City's Land Development and Building Code.

Approved Budget: \$1.6 million (All Incentive Programs) Expenditures to Date: \$0

#### **Completed Tasks:**

June 14 Applications in Progress; 3 Application Submitted/In Review; 2 Applications

Approved. Ribbon cutting ceremony held June 22nd for East of Chicago

July 16 Applications in Progress; 4 Applications Submitted/In Review: 2 Applications

approved

August Status of Program Application - (5) In Progress; (2) Submitted/In Review; (5) Incomplete;

(5) Cancelled; (2) Inactive; (2) Approved

September Status of Program Application - (6) In Progress; (1) Submitted/In Review; (2) Approved;

(4) Incomplete; (6) Cancelled; (3) Inactive

October Status of Program Application - (6) In Progress; (1) Submitted/In Review; (2) Approved;

(4) Incomplete; (6) Cancelled; (3) Inactive



## **Demolition Program**

**Scope of Work:** The Demolition Assistance Grant Program is intended to support economic development and growth in the South Cape area by providing financial assistance to property owners who are committed to improving their properties through demolition projects and preparing parcels for modern development.

**Approved Budget:** \$1.6 million (All Incentive Programs) **Expenditures to Date:** \$0

#### **Completed Tasks:**

June No activity to date
July No activity to date
August No activity to date
September No activity to date
October No activity to date



# Thank you Any Questions?

